



Shasta Lake Water Resources Investigation

**Anadromous Fish Survival and
Water Supply Reliability**

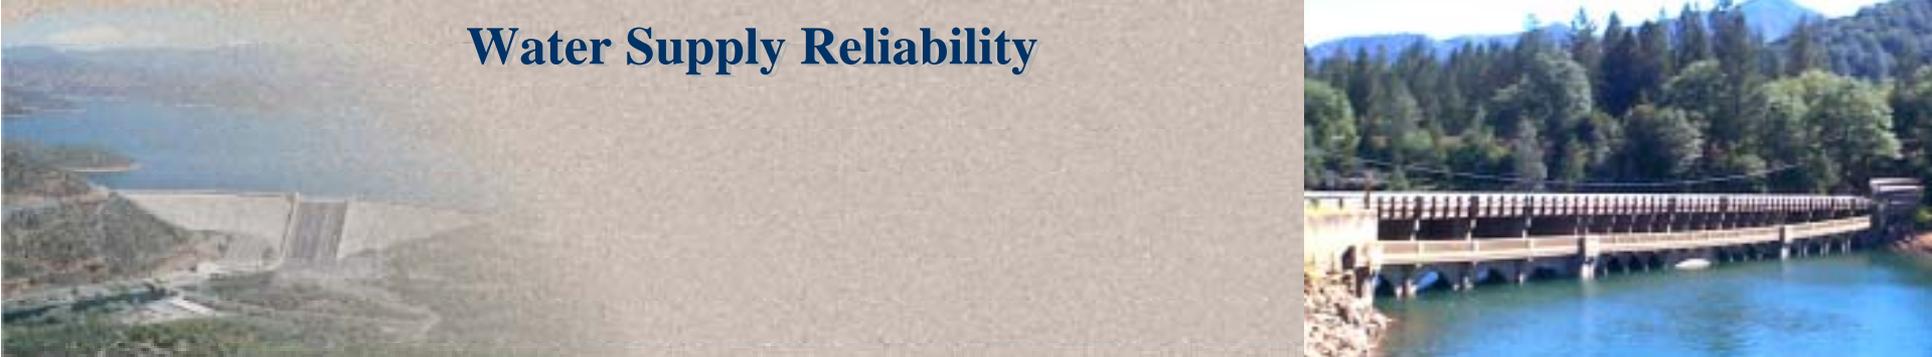

ROD SCHEDULE

Task	Completion Date
Resolve legal issues to allow State agency cooperation	Dec 2000
Complete feasibility study and preliminary design	Dec 2003
Complete environmental review and documentation, obtain Federal authorization and funding, and begin construction	Dec 2004

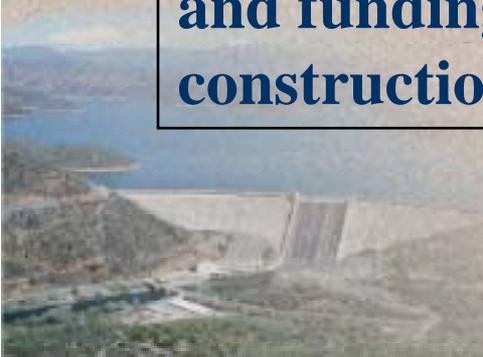

CURRENT SCHEDULE

Task	Completion Date
Complete Plan Formulation Strategy/ Mission Statement Report	Mar 2003
Issue NOI/NOP	Jun 2003
Complete Alternatives Information Report	Dec 2003
Complete draft feasibility report and EIS/EIR	Dec 2005
Complete final feasibility report and EIS/EIR	Jun 2006

Issues

- **Lack of federal funding in years 1-3 has caused delays to the study schedule**
- **Projected year 4 funding may be less than sufficient to maintain current schedule**

